ITB 8 [illegible]

App. F. IX-4

1955-56
(I.T.B.)

File No. 13-55

Serial Nos. 12,

Previous References.

ITB 25 49-5, 6
ITB 40 49-5, 6, 7, 8

Later References.

LH 161 CTB 57

GENERAL AND REVENUE SECRETARIAT

Serial Nos. 8-58

Part B for June 53

SUBJECT

Revised Estimate for the North Zone of the Industrial Suburb, Bangalore

WD 01425—GPB—25,000—15-9-1952.

Order No. L 3016-20/D. 18-6-53

To,
The Chairman, C.D.T.B. B
The Chief Engineer
The D C. Bangalore
The Controller S.A.D

14/7/55

Sanctions the revised estimate for Rs 14, 25,000

APP. F. III—1]

(P1)

GENERAL AND REVENUE SECRETARIAT.

1736/

( )

NOTES.

File No.

FILE HEADING.

FROM The Chairman cum, Bangalore Trust-Board

No D.S.N.J. 228/57-58 Dated 7—6—57 Received.

Diary No.	Enclos.	Spare copies	Serial No.

BRIEF ABSTRACT OF LETTER

Revised estimate for the work connected with the Domestic Water Supply, Bangalore

NOTES AND ORDERS.

submitted the revised estimate for Rs 14,30,556/- for the above work may be sent to the Deputy Chief Engineer unofficially for favour of scrutiny & early return

Mr 12/6 Sd/- 2. 12-6-14/6

3 Mr

Sd/-

(P2) 1735/ml

No. of 194 | General and Revenue Secretariat

U.O. 81 dated 27-6-57
4. Forwarded to the Deputy Chief Engineer for favour of scrutiny of the estimate & early return
Bangalore 23.5.57
Demi-official & secretary to govt. Dy Deptt. D. 3-11-51.

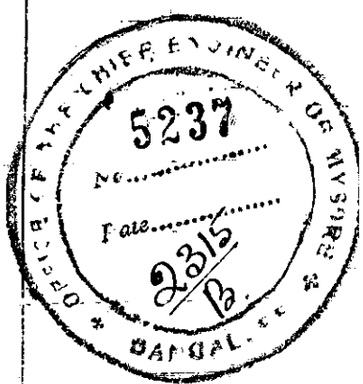

U.O.No. 453 one file.

Returned to the Secretary to Government, L.S.G. Department.

5. The following particulars may be called for with relevant records in support of the provisions made in the estimate as otherwise the estimate enclosed is not susceptible of scrutiny or verification:

(a) Detailed cost datas are to be furnished in respect of the rates for burnt stone slab drains, stoneware pipe shoulder drains and L-shaped drains.

(b) Detailed estimates for the works are necessary

(c) As the work of formation of the layout is reported to have been completed, except for the item of tarring roads, detailed measurements as per actual execution may be furnished.

(d) Detailed drawings (such as longitudinal and cross sections, plans etc.,) are necessary for verifying the quantities provided in the estimate.

(e) The original alignments of the roads behind Yeswanthpur Soap Factory, the Chord Road etc., and the proposed deviations are not marked in the plan

28/6 PRR 28/6 6/7/51 24/10/51

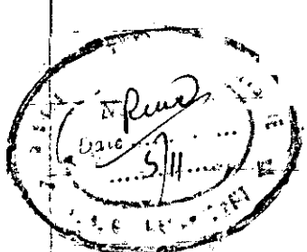

5/XI 5/11

(P3) Revised estimate for the North Zone — Industrial suburb, Bangalore 1733/1

(f) Further, it is seen from the estimate that the roads in the layout are distinguished by several alphabets thus AB, BC and so on. But as these are not marked in the plan, the road lengths cannot be verified.

(g) A plan complete in all respects is necessary to facilitate proper scrutiny of the estimate.

(h) A sum of Rs.27,672/- is provided for forming an approach road. No measurements or detailed estimates are furnished except a data sheet for Rs.7-3-0 per Rft. of roadway.

(i) Lumpsum of (1) Rs.1,450/- for a C.I.pipe sluice for the tank bund, (2) Rs.5,000/- for planting avenue trees and (3) Rs.5,000/- for survey charges and marking the sites, are made in the estimates. Detailed estimates together with drawings wherever necessary, are to be furnished.

(j) A sum of Rs.23,300/- is provided for towards the construction of Inaugural Pillar and its connected works with the remarks "as per detailed estimate submitted to Government for sanction". The sanctioned estimate may also be enclosed.

kkm.

N. Ramaswamy
Chief Engineer of Mysore.
1/11

6 A draft letter is put up calling for the above particulars
17/11

7 Issued
19/11

To The Ch. Dr. Bd. Bangalore
No. L. 9174/22/11/51
Calls for certain particulars

8 Submitted with a draft D.O reminder
for approval

(P4) Revised estimate for North 2nd of the Industrial Estate

1735 ||/1

To

The Ch. Ex. Bd. Bangalore

No. L. 12597/8/L/52

Reminds.

Letter No. G 969/53-54 dt 20/3/52 from the Chairman, B.T.B. in the matter

to submit the same may now be sent to the Chief Engineer for favour of scrutiny & early return with reference to the note in para 5 above

21/4

SMA 21/4/52

Yes

22/4

E.O No. 321 Dt 24.4.

H73-S

28-4-52

319

B

forwarded to the Chief Engineer for favour of scrutiny and early return

Sri B.K.A

BB No. 111.

1/5/52

Sri C

R.K.B

29/4

29/4 with file 1/35.4

B.I with file

B.O

SMA 23/4

Dy Secretary

(P4)

U.O.FILE No.32 dated 24-4-1952 from the Secretary to Government, L.S.G. Department, Bangalore, regarding revised estimate for the North Zone of Industrial Suburb Bangalore.

Memo No. 193 / 1 file Dated 4-8-52

Retransmitted.

12) The revised estimate for the above work is scrutinized for Rs.14,28,200/- subject to the following observations:-

(1) It is stated by the Chairman, City Improvement Trust Board that Government in their Order No.L.13646/MI dated 19-2-1948 accorded sanction to specific rates to be adopted in carrying out the work on piecework system. Neither a copy of the G.O. nor a copy of the approved schedule is to be found in the file. Therefore, the rates provided for in the estimate are retained without making any corrections with reference to the approved schedule of rates of the Trust Board for the year 1951-1952. Whether there are any differences in the rates sanctioned by Government and the Schedule rates will have to be ascertained from the Chairman.

(2) With regard to the rate for soling metal, it is stated that, as the rate of Rs.3-14-0 per Cyd. approved by Government is not workable, a rate of Rs. 5-8-0 per Cyd. (said to have been approved by the Trust Board) is provided in the estimate. But, the approved schedule of the Trust Board provides for a maximum rate of Rs.4-8-0 only per Cyd. On what authority the higher rate is provided is not clear.

(3) The quantities provided in the estimates for layout portion do not admit of any verification at all as detailed drawings showing the levels of the proposed roads, longitudinal and cross sections etc., are not furnished. It is stated by the Chairman of the Bd that the drawings are not available at present an

Revised estimate for Northern zone of the Industrial Suburb

V/52-53/mel

that the quantities furnished by him are all as per actuals. Even then there should be detailed plans to check the estimates, whether the original plans have been modified in any way is not stated. The estimates for the layout portions are, therefore, checked only arithmetically.

(4) Likewise, with regard to the several masonry culverts, detailed estimates are no doubt furnished; but in the absence of detailed drawings such as longitudinal and cross sections, plans etc., the quantities provided in the estimate do not lend themselves to any check.

D.S. Venkanna

The Secretary to Government,
Local Self-Government Department

(D.S.VENKANNA)
Chief Engineer of Mysore.

IS

5/8/52

13) Submitted with draft letter to get the above particulars

9/8

11/8

14) Issued

11/8

To

The Chairman,
B-T-B

L.7399/B.T.B.8-52-25 dt 18-8-52 -- calling for a report

Sri A

15) Reminder no. L. 14447 dt 25-11-52

(P7) V. 8346. Revised estimate for the work in Zone of the Industrial colony

Letter No. A2.P.R.288/52-53 & 51-1 from the chairman, Bangalore Town Board on the subject

16) This may be sent to the Chief Engineer with the particulars now received from the chairman with reference to his note in para 12 above

E.O No. 348 Dt 25-2-53

Ma 14/2. SDO 16/2

17. Forwarded in duplicate to the Chief Engineer in Mysore Block for favour of further action & return

Dy. Secy Lib 28/2

Dr. IV 5/262/53 27.2.53

717 No 2653 3-3-53.

27/2

27/2/53

T.O. 4/3/53 4/3

U.O.No. 491/RB-53-54 dated, 15-4-53.

Retransmitted to the Secretary to Government, L.S.G. Department.

18. The estimate is now scrutinized for Rs.14,28,200/-

(a) A rate of Rs.0-5-6 per Cft. of "unsized stone paving" is provided for the floors of culverts and data in support of the rate proposed has to be got approved.

(b) A rate of Rs.5-8-0 per Cyd. for soling metal for roads is retained, as the rate is stated to have been approved by the Board in their meeting held on 21-12-1948.

SECRETARY TO GOVT. L.S.G. DEPARTMENT 16 APR

K.S.Gangadharam (K.S.GANGADHARIA) 15/4/53

LS/15-4-53. Chief Engineer of Mysore.

19. For orders whether the information may be called as to the approved rate for the works referred to in (a) & (b) in schedules of the Board for the period

16/4

8346/Rev Revised estimate for the
(P3) work Zone of the Executive Sahib
during which these works were
executed, together with an extract
of the schedule showing these rates
Mo 27/4 20. Do they included in the four year
Programme
8/5 30/4
3/5

21. Submitted with reference to para 20 above
this is included in the four-year programme.
The work is under execution & a few
items have also been disposed of
Mo 5/5
22 The information said to have
8/5 6/5 been required could be found
in the Comparative Statement in the
field pl verify & continue the note
further please, note the amount
spent so far for this scheme
9/5

23) Submitted please see the Chief Engineer's
note in para 12(a) the rate of soling metal
is Rs 3-14-0 cft (minimum) + Rs 4/- Maximum.
But the Board has offered to give Rs 5-8-0 for the cft
for this item of work this has to be got clarified

24) As regards the rate of 0-5-6 per cft for
"Un sized stone pitching" — it is not clear
what the minimum rate & the maximum rate
of the schedule are & what the sanctioned
rate in the original estimate is

25) Though attempts is made to note these

8346/ml Revised estimate by the WE the 2 nos of the Indus that submit

details from the abstract cumulative statem

it could not be found when these items are

provided it is perhaps desirable to get these

particulars from the Chairman before the

estimate is sanctioned, as the Chief Engineer

Vide para 18(a) suggests that the ratio ibid be observed.

6) As regards the expenditure incurred

in this year, the latest statement received

from the Chairman shows that a sum of

Rs 9,16,813-10-1 has been drawn by the

Trust Board upto the end of March, 1953

The revenue with reference to

para 22 above

5/6. 27) The Bd has approved a rate which is

T Ch more than the maximum that seems

8/6. to be highly irregular. (Vide Para 23).

It is strange why the office of the Chief

Engineer has not objected to this. However

it is better to enquire from the Chairman

how the Bd approved the rate of Rs 5-8-0

as against Rs 4-00 the maximum

Other details should be called for

Secy dcf)

28) Yes and very soon

11/6

29) A draft letter is put up for approval

15/6

30) Issue

16/6

SECRETARIAT GOVERNMENT 2025 9 JUN 1953 PUBLIC DEPARTMENT

(P10) 8346/ml ✓ 6763

Revised estimate for the works done of this undertaking Scheme.

To

The Chairman, C.I.T.B, B'lore

No. L. 3951/C.I.T.B. 8-52-54 dt 3.2.53

called for further information

Secs. A. 3.2.53

Reminder 13004 dt 6-1-54 ch C.I.T.B

Letter No 4369/53-48 (8-1-54.

from the chairman, C.I.T.B.

31) This will be sent to the chief Engineer for further remarks in the light of the information furnished by the chairman, with reference to his (chief Engineer's) remarks ~~in para~~ under para 1& above

— Ref para 2 & above

The records received from the chairman are also flagged.

No 2/2.

32) Yes

Sec 2/2 Q.O.No. L-264 dt 8.2.54

2682

RB 8331

13.2.54

33) Forwarded to the chief Engineer for remarks & early return

Asst. Secy, Fin & Planning Depts

Sec 5/2

B. IV Sec

Sec PAR Engrs

16/2/54.

10.2.54

DA 739 16/2/54.

10/2/54

17/2/54

Secretary.

18/2

(P11)

PUBLIC WORKS DEPTT., SECRETARIAT. File No. of 194

Serial No.

U.O.No. 10487/RB-53-54 dated, 12.3.54.
Encl. 1 no. file with Estimate & records 18
1. Retransmitted.

34. The approved Schedule of rates of the City Improvement Trust Board for 1951-52 provides for a maximum rate of Rs. 3/- per cyd. (or Rs.0-2-0/cft.) of unsize stone paving. But, a rate of Rs. 0-5-6per Cft. is seen to have been provided for in the estimate. The data sheet furnished in respect of this item of work is not susceptible of any check since details as to the size of stones used, the lead involved, the actual labour employed & etc., are not noted therein. Therefore, a rate of Rs. 5-0-0 per C.yd. (stated to have been provided for i the original sanctioned estimate) is allowed and the rates corrected accordingly.

or Rs.9-4-6/cyd.

A

By para receipt

35. As regards the rate of soling metal for roads, the approved Schedule of rates of the City Improvement Trust Board for the year 1951-52 provides for a maximum rate of Rs. 4-8-0/per cyd. Only this rate will have to be paid for in the absence of any quotations, which ought to have bee the basis of the Board's resolution. But, it is stated that a data-sheet for Rs. 5-8-0/ per cyd. was got approved by the Board and that this rate was adopted in the Schedule of rates for the year 1949-50 for which sanction of Government was obtained. Neither a copy of the approved data-sheet nor a copy of the approved Schedule for 1949-50 is available in this office. Hence the rate of Rs. 5-8-0/per cyd is retained, pending

B

p.t.o.

WT 0109-1—G PB—20,000—25-2-41

(P12) Revised estimate for the North Zone of the Industrial Suburb, Bangalore

6763/Mel

pending verification with the Schedule.

36.) The total estimated cost of the work is corrected to Rs. 14,27,000/-.

Secretary to Government,
L.S.G. & Planning Deptts.,

Secretary
17/3
(H.C.K.BHATTA)
Deputy Chief Engineer.

37) In orders whether the estimate may be sanctioned for Rs 14,27,000 pending further clarification as to why higher rates were paid in respect of items referred to in paras 34+35 above

Mca 24/3

38) Get data sheets + further info as noted at A to B

SDO 25/3

24/3

39) Draft letter is furnished

Mca 2/4

40) Issue

SDO 3/4

7/4

-10,

The Chairman, B.T.B.
Lr 28 L dt/4/74.
calls for certain information

Secy Adm

SDO

(113)

Revised estimate for the North Zone of Industrial Suburb B'lore 6768/mg J 6384-

V7292

41) Reminder is sent up
26/1

42) Issued
R.No L 5445 dt 10-8-54

43) Reminder is sent up
8/11

44) Issued
R No L 10613 / dt 4-12-54

Letter No 1430-/54-5 dt 22-12-54 from the chairman, BTB

45) The information was furnished by the chairman, Bangalore Water Board, in his letter dt 22-12-54 (page) it may be sent to the C.E. with reference to his note in paras 34 and 35 of the notes

2820
RB 9656
1711

Memo is further accompanying

30/12 1/1

Now the letter dt 4-1-55 from the chairman

This is also further (P.27)

46) E.O No L. 247

28/12-1-55

47) Forwarded to the chief Engineer for remarks and early return

Asst. secretary
Elec & Leg Depts.

Bx. IV

5ni 8?
9/1/1/55
RNo 685
22.1.55

C.E
15.1.55

M
25/1/55

7290 (P14) Revised estimate for the work 2 we — Industrial suburb.

U.O.No.1308 /RB-54-55 Dated, 5th Feb.1955.

Encl. 1 no. file

Retransmitted.

48) The estimate is scrutinised and corrected to Rs. 14,27,000/- in the light of the information furnished by the Chairman, City Improvement Trust Board, Bangalore.

49) It is seen that a rate of Re. 0-5-6 per Cft. or Rs.9-4-6 a cyd. is provided for unsized stone paving in the estimate. The approved schedule of the City Improvement Trust Board, for the year 1951-52, provided for this item of work, a rate of Rs. 3/- per cyd., which is also the rate provided for in the schedule of Buildings Division, Bangalore, for the year 1950-51-52. As a special case, the rate originally provided in the estimate i.e., Rs. 5/- per cyd. has been admitted and nothing more than this is admissible.

50) With regard to soling metal for roads a rate of Rs. 5-8-0 per cyd. is provided for in the estimate and this rate is retained as it is stated to have been approved by Government in their Order No.L. 9696/40-49-6 dated 14-3-1950.

Secretary to Government,
L.S.G. Department,
Bangalore.

(L.C.MUNISWAMY REDDY)
Deputy Chief Engineer.

IS/2-2-55.

51) The revised estimate may forthwith be sanctioned for Rs 14,27,000 as scrutinised by the Deputy chief Engineer.

52) Please examine the points noted in Para 49. How was a rate more than the Scheduled Rate provided and accepted How much will be the excess on account of this Rs 5/- accepted by Govt. Was not the C.E Consulted there These points should be examined

(P13)

Revised estimate for the North Zone of Industrial Suburb B/Line 6768/ml. 6884-

√7292

41) Reminder is sent up
Es 26/1

42) Issued
R.No L5445 dt 10-8-54

43) Reminder is sent up
Es 4/11

44) Issued
R No L 10613 / dt 4-12-54

Letter No 1430/54-5 dt 22-12-54 from the chairman, B.T.B

45) The information was furnished by the chairman, Bangalore Road Board, in his letter dt 22-12-54 (Page) it may be sent to the C.E. with reference to his note in paras 34 and 35 of the notes.

2820
RB 9656
1711
Another letter dt 4-1-55 from the chairman. This is also furnished (P.27)
Ms

Memo is furnished accordingly
30/12 1/1

46)
E.O No L 267
1/1

47) Forwarded to the chief Engineer for remarks and early return

Asst. secretary
Estb. & Leg Sects

Ms
25/1/55

Ms
B.IV

Sri BC.
17/1/55
RNo 685
20-1-55

C.E
15.1.55

dt 13/1/55.

7290 (P15) Revised estimate for the work
8830 Laying of the Industrial Subway

Letter No 7914/54-5 & 28/2/55 from the Chairman, B.T.B

Vide sl. No 19 the statement page 26.

53) As seen from the statement (page 26) received from the chairman, Rs 5/- for c.y. cubic yard was provided in the estimate (original) which was sanctioned in GO No 4781-7/RL 171-48-2 & 5-11-48, as scrutinised by the then Deputy chief Engineer for Roads and Buildings. According to the note in para 49 of the notes, the Deputy chief Engineer is for retaining the rate of Rs 5/- c.y. as against Rs 9-4-6 a c.y. as proposed by the chairman — Ref para 52 in the previous page.

Fly H.

Ma 18/3 S.O. 19/3

54) The opinion of the Deputy chief Engineer at Paras 48, 49 and 50 may be agd. The revised estimate may be sanctioned for Rs 14,27,000 as scrutinised and corrected by the D.C.E.

6/4

Secy Edn 7/4

55) What is the position?

7.4.55

Vide portion marked 'A' in page 6

56) The cost of the revised estimate is Rs 14,27,000 as against which, a sum of Rs 19,27,917

EDUCATION SECTION
422
7 APR 1955
GOVERNMENT OF MYSORE

8830
MH (P16) Revised estimate for the North Zone of Industrial Suburb

is expected to be realised from sale of sites, leaving a profit of Rs 5,00,000. The cost of the work will be debited to the provision made in the budget of the Board for this scheme year after year till the work is completed — Ref para 55 overleaf

Ma 18/4 20/4

57) [signature]
20/4

Secy (Edn Deptt)

EDUCATION
1162
21 APR 1955
GOVERNMENT OF MYSORE

58) Para 54 may be adopted

[signature]
21.4.955

Minister (Edn)
Chief Sec'y)

FINANCIAL SECRETARY
GOVT: OF MYSORE
22 APR 1955
U. O. No. 944 Fl.

~~It should be noted that the rates to be fixed for the sites sold are to be fixed~~

(59) 23/4 (78)

[signature]
26/4/55

[signature]
26/4

11 MAY
MYSORE

60)

[signature]
11/5/55

P.
11.5.55

[signature]
12/5

OFFICE OF THE MINISTER FOR
PUBLIC HEALTH & LOCAL-SELF
GOVERNMENT.
25 APR 55
No. 576.

61) Draft gois finalised
Ma 3/6.

62) Putting up typed draft

[signature]
5/6

(P17)

Revised Estimate for the Work Zone of Industrial School 8830 Rs.

Submitted:- Typed set is put up for kind approval

10/6

EDUCATION SECRETARY
3869
10 JUN 1955
GOVERNMENT OF MYSORE

10/6 Secy (Edn & Labour)

aw
D 11-6-55

Issued to the chairman Alg ITB Blore
C.E. Mysore Blore
Dc Blore Sb
Cuddle SRD Blore

L 3016-28/ITB-13-53-54/18-6-55

Accordingly Sanction the revised estimate for Rs 14,27000/-

B'
20/6

(1)

C. F. No. 45]

GOVERNMENT OF MYSORE

Telegram/phone

No. 228/ST-2 Encls. 4 files as detailed in last para

OFFICE OF the Chairman,
City Improvement Trust Board,
Bangalore.

Date 7th June 1951.

GENERAL & REVENUE SECRETARIAT
1735
9 JUN 1951
MUNICIPAL BRANCH.

To

The Secretary to Government,
Local Self Government Department,
Bangalore.

Sir,

L. S. G. DEPARTMENT

Subject: Revised Estimate for the North Zone of the Industrial Suburb, Bangalore.

Adverting to Government Order No.L.4781-7/Ml. 171-48-7 dated 5th November 1948 sanctioning a scheme for the formation of the Layout viz., the Industrial Suburb, North Zone, at an estimated cost of Rs.8,21,600/-, I write to state that the work has been taken on hand and gone through to a considerable extent. The Engineer Officer of the Board has submitted a Revised Estimate for the work in question. The Revised Estimate amounts to Rs.14,30,556/-. Government in their Order No.L.13646/Ml. dated 19th February 1948 accorded sanction for specific rates to be adopted in carrying out the work speedily on piece-work basis and these rates have been adopted in getting up the Revised Estimate.

The work in connection with the formation of the layout has now been completed except for the tarring of roads which is also to be taken up. The revised cost for the formation of Roads will amount to Rs.4,39,442/- as against the sanctioned provision of Rs.3,10,665/- . This excess is due to the fact that the rates provided in the original estimate for earthwork and soling metal were out of date, and unworkable and piece-work rates had to be adopted.

During execution the alignment of 40' Road behind Yeswant Soap Factory has been slightly modified to avoid the roads running across deep scours, the formation of which would be very costly. The 40' Road joining the 80' Road and the chord road running along

along the foot of the Hillock has been avoided as it would serve very little purpose while costing considerably. Some minor changes in the formation have also been adopted in order to give access to the sites facing East.

Provision had been made in the sanctioned estimate for metalling of roads to a width of 16' and as this was found to be inadequate to cope with heavy traffic that would be passing here, a mettalled width of 18' has been adopted.

As against a rate of Rs.3-12-0 provided in the sanctioned estimate for supplying of soling metal a rate of Rs.5-8-0 per c.yd. has been now provided as per decision of the Board.

The cost of the Inaugural Pillar standing 35' and costing Rs.8,000/- as also the cost of forming a park alround has been included in the present estimate as per orders. Provision has been made for the maintenance of the above works till they are handed over to the Corporation.

As against the sanctioned provision of Rs.3,55,971/- under Land Acquisition charges a provision of Rs.5,70,114/- has now been made in the revised estimate, as per details furnished by the Special Land Acquisition Officer of the Board.

A provision of Rs.2,66,000/- towards conversion fine to be paid towards conversion fine at Rs.2,000/- per acre has also been made in the revised estimate. Provision for Water Supply arrangements has been retained as per the sanctioned estimate.

As against the original proposal to form 144 factory sites of varying dimensions, 148 sites have been actually formed.

This figure includes the 17 sites by the side of the Tumkur Road that have been reserved by the Government. The additional extent of 25 acres and 20 guntas of land situated by the side of Tumkur Road has been taken over from the Gopala Rao Enquiry Committee.

As against the expenditure of Rs.14,30,556/- a realisation of Rs.19,27,917/- is expected leaving a profit of Rs.4,97,361/- which works out to 34.83 per cent.

The report of the Engineer Officer accompanying the revised estimate explains in detail the necessity for the provisions made and deviations from the original sanctioned estimate. The subject was placed before the Board at its meeting held on 27th February 1951, when it was resolved:-

> "That the revised estimate for Rs.14,30,556/- for a scheme pertaining to the formation of the Industrial Suburb, North Zone be approved".

I request in these circumstances that orders of Government sanctioning the revised estimate may kindly be communicated.

The following enclosures accompany:-

1. Revised estimate for Rs.14,30,556/-,
2. Report accompanying the estimate,
3. Comparative Statement showing the difference between the sanctioned General Abstract and the revised Abstract Estimate for the layout in question,
4. Data sheets.

Yours faithfully,

H.V. Narasimhaiah

Chairman.

AMD.2.

(6)

Rs.~~19,27,917/-~~ (14,30,556/-) for which a realisation of Rs.19,27,917/- is expected leaving a profit of Rs. 4,97,361/- which works out to Rs.34.83%.

x Mus is corrected Rs 14,27,000/-

The Revised Estimate may kindly be placed for before the Board and obtain sanction of Government.

(Sd.) R. Madhavan,
Engineer Officer.

"Copy"

CHAIRMAN.

G. R. S. App. F. G. 3]

GENERAL AND REVENUE

SECRETARIAT.

(*Continuation sheet draft form.*)

Subject Revised estimate for the ~~work~~ North Zone of the Industrial Suburb

~~Sir~~, L 9174/Gen Records

To, 22 / 11 / 54

The Chairman,

C.D.T. Board,

Bangalore

Sir,

With reference to your letter No. G. 288/5752 dt 7-6-57 on the above subject, I am directed to request you to ~~forward~~ send the following particulars ~~in the matter~~ with relevant records in support of the provision made in the estimate

1) detailed cost data in respect of the rates for burnt stone slab Rains;

2) detailed estimates for the works;

3) detailed measurements as per actual execution of the work of formation of the layout ~~which~~ is already completed;

4) detailed Rainings (Mech

WD 010855—GPB—25,000—18-7-59

as longitudinal & cross sections, plans etc) for verifying the quantities provided in the estimate

5) The original alignments of the roads between Yesvanthpur soap factory, the chord road etc and the proposed deviations may be marked in the plan, as they are not marked now,

6) The roads in the layout are distinguished by only ~~after~~ alphabets as like A B, B C & so on and, they are not marked in the plan, the road lengths cannot be ~~verified~~ verified. This may get done now.

7) ~~A~~ plan complete in all respects is necessary for scrutiny of the estimate.

8) ~~D~~ measurements or detailed estimates for the provision of Rs 27,672/- made for forming an approach road

9) detailed estimates ~~together~~ together drawings wherever necessary, for the following provisions made :-

(a) Rs 1450 for a c.i. pipe sluice for tank bund;

(b) Rs 5000 for planting avenue trees

(c) Rs 5000 for survey charges & marking the sites

10) the sanctioned estimate for Rs 23,300 for the construction of inaugural pillar & its ~~connected~~ connected works

Records accompany for necessary action & return with the above

must for the [illegible] 1911

9463 8-52-24

C. F. No. 45]

GOVERNMENT OF MYSORE

1 APR 1952

OFFICE OF THE MUNICIPAL BRANCH

T [illegible] ram
[illegible] phone.

No. G-969/51-2 Encls. (2) files.

The Chairman, City Improvement Trust Board, Bangalore.

Date 20th March 1952.

To

The Secretary to Government,

Local Self Government Department,

Sir, Bangalore.

Subject:- Revised Estimate for the North Zone of Industrial Suburb.

With reference to your No.9174 dated 22-11-51 returning the above estimate with observations and asking for certain information I herewith transmit the revised estimate duly furnishing particulars asked for. The following are enclosed.

1. The detailed cost of the scheme and the Data sheets with cross sections of the burnt stone slab.

2. Detailed estimate for the works.

3. Detailed measurements as per actual execution of the work of formation of the Layout already completed.

4. The levels of the proposed roads were taken at the time of execution to fix up only the gradients and to give formation levels only. These drawings are not available at present. The entire work was taken upon piece work system and all the works have been measured finally and enclosed checkmeasured by the Assistant Engineer and some cases by the Engineer Officer. The quantities of measurements now furnished are all as per actuals and taken from the commencement.

5. The original layout plan marking thereon the new roads formed.

6. The roads in the layout plan is marked with distinguished letters A, B, C, D with necessary measurements of all the roads.

7. Complete plan showing all the details required for the scrutiny of the estimates is herein enclosed.

8. Copy of the detailed estimate amounting to Rs.27,672/- for forming the approach road.

9. Detailed estimates and plans in respect of the following items of works.

   (a) Estimate for Rs.1450/- for the construction of C.I.pipe sluice for the tank bund in S.No.47 of Yeshavantapur

   (b) Estimate for Rs.5,000/- for planting the Avenue Trees.

P.T.O.

(10) (10)

(c) ~~Xtax~~ Estimate for Rs.5,000/- for survey charges and marking the sites.

(10) Copy of the sanctioned Estimate for Rs.23,000/- for the construction of Inaugural Pillar and its connected works.

The file of papers are all herewith resubmitted for information and early sanction of Government to the Revised Estimate

Yours faithfully,

C.V. Narasimha Rao

(C.N. Narasinga Rao,)
Chairman.

Ksr.

D

(1) (2)

L. 7399 /LTB8-52-28. 18th August 52

L.S.G. Department.

The Chairman,
City Improvement Trust Board,
Bangalore.

Subject:- Revised estimate for the North Zone of Industrial Suburb.

With reference to correspondence ending with your letter No. 969/51-52 dated the 20th March 1952, on the above subject, I am directed to request you to furnish information on the following points:-

It is stated by you that Government in their Order dated 19th February 1948 accorded sanction to specific rates to be adopted in carrying out the work on piece work system. A copy of the schedule of these rates with information as to whether there are any differences in the rates approved by Government and the schedule rates for 1951-52 may be sent, with a comparative statement.

With regard to the rate for soling metal, it is stated by you that as the rate of Rs.3-14-0 per c.yd. approved by Government is not workable, a rate of Rs.5-8-0 per c.yd. is provided in the estimate. But the approved schedule of the Board provides for a maximum rate of Rs.4-8-0 only per c.yd. Information as to the authority for providing this higher rate may be furnished.

The quantities provided in the estimates for layout portion do not admit of any verification at all, as detailed drawings showing the levels of the proposed roads, longitudinal and cross sections etc., are not furnished. It is stated by you that the drawings are not available at present and that the quantities furnished are all as per actuals. Even then there should be detail plans to check the estimates; whether the original plans have been modified in any way is not stated. Information on this point may be furnished.

In regard to the several masonry culverts, detailed drawings such as longitudinal cross sections, plans etc., besides detailed estimates therefor, are necessary to check the quantities provided in the estimate. This may be sent.

The other plans and estimates accompany for necessary action and return with the above particulars.

Yours faithfully,

(V. HANUMANTHAPPA)
for Secretary to Government,
L.S.G. Department.

LNS.2.13/8.

L 7399/DVB 8-52-25 (13)(12)

18-8-1952 Work Zone of Amritsar estimate for the

Subject

To,

The Chairman, C.I.T. Board,
Bangalore.

Sir,

With reference to correspondence ending with your letter No. F. 969/57-52 & 20-3-52 on the above subject I am directed to request you to furnish information on the following points :—

It is stated by you that Govt. in their order Ld 19-2-48 accorded sanction to specific rates like adopted in carrying out the work on piece work system. A copy of Schedule of these rates with information as to when there are any differences in the rates allowed by Govt. & the Schedule rates for 57-52 may be sent, with a comparative statement.

With regard to the rate for soling metal, it is stated by you that the rate of Rs 3-14-0 per cyd allowed by Govt. is not workable, a rate of Rs 5-8-0 per cyd is provided in the estimate but the allowed Schedule of the Board provides for a maximum rate of Rs 4-8-0

(13) ~~14~~

~~only for copy information as to the authority for framing this higher rate may be furnished~~

only for copy information as to the authority for framing this higher rate may be furnished

The quantities framed in the estimates for layout portion do not admit of any verification at all as detailed drawings showing the levels of the proposed roads, ~~logitud~~ longitudinal & cross sections etc are not furnished It is stated by you that the drawings are not available at present & that the quantities furnished are all as per actuals Even then there should be detailed plans to check the estimates; Whether the original plans have been modified in any way is not stated information on this point may be furnished

In regard to the several masonry culverts, detailed ~~estimates~~ drawings ~~are necessary~~ such as longitudinal & cross sections, plans etc, besides detailed estimates therefor, are necessary to check the quantities framed in the estimate this may be sent

The other plans & estimates accompany for necessary action & return with the above particulars.

yours faithfully
11/8
Asst Engr

ITB 8-52-51

F. No. 45] **GOVERNMENT OF MYSORE**

Tele gram phone

OFFICE OF the Chairman,
City Improvement Trust Board,
Bangalore.

R.No. 288/52-53.
Encls. 1 Estimate Carrying 28 leaves
2 Drawings
4 Tracing of Longitudinal and Cross Sections

Date 2nd January 1953.

To

The Secretary to Government,
Local Self Government Department,
Bangalore.

Sir,

Subject: Revised estimate for the North Zone of Industrial Suburb.

With reference to your No.L.7399/ITB.8-52-5 dated 18th August 1952 regarding the above, I am herewith submitting the following particulars for your information.

1. Comparative statement showing the difference between the sanctioned rates provided in the estimate and the sanctioned schedule of rates for 1951-52 is herewith enclosed for information. The copy of the sanctioned rates is herewith enclosed.

2. A rate of Rs.5-8-0 to Rs.6/- per c.yd., for the soling metal is provided in the estimate as per approval of the Board in the meeting held on 21-12-48 and a copy of the resolution is herein enclosed. This rate has been provided in the schedule of rates for the year 1952-53.

3. The sanctioned layout plan and the revised layout plan showing the proposed new roads with clear dimensions are herein enclosed. Longitudinal and cross-section for the marginally* noted roads are herein enclosed.

* 1. 60 ft. road A to B commencing from Tumkur Road - 2250 ft.
2. 60 ft. road C.T.commencing from the Junction of Chord Road. - 1675 ft.
3. 60 ft. road D.T. -do- -do- - 1098 ft.
4. 80 ft. road H.G.commencing from pipe line to Chord Road (H.G.1 to G2 and G) including loop. - 1950 ft.
5. 60 ft. road K.J.commencing from pipe line to near overbridge. - 2400 ft.
6. 60 ft. road L.T.commencing from Tumkur Road to Mahalakshmi Mills. - 1850 ft.

P.T.O.

(15) (16)

4. As regards to the detailed drawings for culverts the section of the culverts have been noted on the copy of the respective estimates only and they are all as per actuals and may be admitted.

Yours faithfully,

(R.Madhavan)
Chairman.

AMD.

(17-16)

Office of the Chairman,
City Improvement Trust Board
Bangalore.

Proceedings of the Meeting of the City of Bangalore Improvement Trust Board, held on 21st December 1948 at 4 P.M.

Engineer Officer's letter dated 11-12-48 stating that the rate of Rs. 5-8-0 per Cyd of soling metal approved by the Board in respect of Industrial Suburb North Zone is not workable in the case of other Extensions viz., Jayanagar Extension and Housing Area in the Industrial Suburb and that according to the data furnished, a rate of at least Rs. 6/- per Cyd may be given to the Contractors etc.

"Resolved that the Engineer Officer's proposal to pay for the soling metal for roads in the Jayanagar Extension and and the Housing Area in the Industrial Suburb at the rate of Rs. 6/- and Rs. 5-8-0 per Cyd in the Industrial Suburb North Zone in the circumstances reported by the Engineer Officer, be approved.

(Sd) C.N. Narasinga Rao,
CHAIRMAN.

Copy

D.S.R.Rao
27/12/48

Engineer Officer,
City Improvement Trust Board
Bangalore.

G. R. S. App. F. G. 3.

GENERAL AND REVENUE SECRETARIAT

(*Continuation sheet draft form*).

L 3951 9-3-8-52-59

3-7-53 ~~18~~ (17)

Re:- Revised estimate for the Western Zone of Industrial Schools

To,

The Chairman, C.P.T. Board, Bangalore

Sir,

With reference to correspondence ending with your letter No A2 PR 285/52-53 dt 31-1-53 on the above subject, I am directed to state that a rate of Re 0-5-6 per cft of unsized stone facing" is provided for the floors of culverts & Data in support of the rate proposed has to be explained.

Again a rate of Rs 5-8-0 per cyd for filling metal for roads is provided, as the rate is stated to have been offered by the Board

Dc.
3/7

WD 01417—GPB—25,000—3-11-52

(18) ~~(9)~~

at this meeting held on 21-12-48 When the maximum rate of Rs 4/- how a rate of Rs 5-8-0 was ~~given~~ provided was not explained. I am to request you to furnish information on the following points with information as to the reasons & approval for adopting the rates other than those provided in the original estimates or in the schedule

~~(1) [illegible]~~

		Rate provided in the sanctioned estimate	Schedule rates	
			Minimum	Maximum.
(1)	Un sized stone facing " for the floors of culverts	—	—	2 —

— the total excess cost involved at the rate now fixed 3

(2) Spring metal for Roads — Do — Do — Do

Records accompanying for reference & return with the reply

~~Yours~~ Yours faithfully

Asst Secy 21/

8a

MS 21/7/53

~~20~~ (19)

Mysore Government
xxxxxxxxxxxxxxx/

L.3951/9%3 8-52-59

3rd July 53

The Asst.
L.S.G. & Planning Departments

To

The Chairman,
City Improvement Trust Board,
Bangalore

Sir,

Subject:- Revised estimate for the North Zone of Industrial Suburb.

With reference to correspondence ending with your letter No.A2. P.R.288/52-53 dated the 31st January 1953, on the above subject, I am directed to state that a rate of Re.0-5-6 per c.ft. of "unsized stone paving" is provided for the floors of culverts and data in support of the rate proposed has to be explained.

2. Again a rate of Rs.5-8-0 per c.yd. for soling metal for roads is provided, as the rate is stated to have been approved by the Board at their meeting held on 21st December 1948. When the maximum rate is Rs.4/- how a rate of Rs.5-8-0 was provided may kindly be explained.

3. I am to request you to furnish information on the following points with information as to the reasons in having adopted and approved the rates other than those provided in the original sanctioned estimates or in the schedule:-

	Rate provided in the sanctioned estimate	Schedule Rates Minimum	Schedule Rates Maximum
	1	2	
(1) Unsized stone paving for the floors of culverts.			
	The total excess cost involved at the rate now provided.		
	(3)		
(2) Soling metal for roads	-do-	-do-	-do-

4. Records accompany for reference and return with the reply.

Yours faithfully,
Hanumanthappa 3/7

(V. Hanumanthappa)
Asst. Secretary to Government,
L.S.G. & Planning Departments.

LNS.2.2/7.

(20)

6763
21 JAN 1954
GENERAL & MUNICIPAL BRANCH.

C. F. No. 63]

GOVERNMENT OF MYSORE

Telegram / phone

OFFICE OF

The Chairman, City Improvement Trust Board, Bangalore.

No. 4369/53-4

Encls 2 data sheets.
1 statement.
1 file of estimates and plans.

Date 13th January 1954.

To

The Assistant Secretary to Government,
Local Self Government and Planning Departments,
Bangalore.

Sir,

Subject:- Revised Estimate for the North Zone of Industrial Suburb.

With reference to your No.L.3951/I.T.B.8-52-59 dated 3-7-53 and calling for certain particulars regarding the - - above I am herewith forwarding the particulars called for as noted below:-

1. The rate of 0-5-6 per C.Ft. for unsize stone paving for the floor of culverts; granite unsize stone paving was done and the rate of 0-5-6 per C.Ft. was arrived at as per data sheet enclosed. In the sanctioned - - estimate a rate of Rs.5/- per C.Yd. for rough stone paving is provided which worksout to 0-3-0 per C.Ft.

   The rate claimed now at 0-5-6 per C.Ft. may be passed.

2. As the rate of Rs.3-14-0 per C.Yd. which was originally provided in the sanctioned estimate for supplying the soling metal was not workable since nobody was coming forward to supply the soling metal at that rate. A data sheet for Rs.5-8-0 was prepared and got approved by the Board after ascertaining the prevailing rates in the Corporation. This rate was adopted in the schedule of rates for 1949-50 and sanction of Government obtained.

3. The required information have been furnished in the form enclosed.

4. All the records sent in your above number are herewith resubmitted.

Yours faithfully,

(R. Madhavan)
Chairman.

Ksr

M. G. S. App. F. G. 3.

MYSORE GOVERNMENT

SECRETARIAT

(Continuation sheet draft form).

WD 03546 —GPB—10,000 —14-8-53

(21)

L 282

12-4-54

To,

The Chairman,

C. I. T. Board,

Bangalore

Sir,

With reference to your letter No 4369/534 dt 18-1-54 re revised estimate for the work of the Industrial Laboratory, I am directed to request you to send the following particulars in the matter

The approved schedule of rates of P.W.D. for 51-52 provide for a maximum rate of Rs 3/- per cft. of masonry stone pointing but a rate of Re 0-5-0 per cft is seen to the

(22) ~~23~~

been provided for in the estimate the data sheet furnished in respect of this item of work is not susceptible of any check since details as to the size of stones used, the head involved, the actual labour employed etc are not noted therein These details may be furnished

As regards the rate of Structural metal for roads, a copy of the approved data sheet ~~was~~ and a copy of the approved schedule may be sent

~~Records~~ Records are ~~forwarded~~ sent herewith for necessary action & return

7/8/54

8/4/54

~~24~~ (23)

L 282

12 April 1954

The Chairman,
City Improvement Trust Board,
Bangalore

With reference to your letter No.4369/53-4 dated the 18th January 1954 regarding revised estimate for the North Zone of the Industrial Suburb, I am directed to request you to send the following particulars in the matter:-

The approved schedule of rates of the Trust Board for 1951-52 provide for a maximum rate of Rs.3/- per c.yd. of unsize stone paving. But a rate of Re.0-5-6 per c.ft. is seen to have been provided for in the estimate. The data sheet furnished in respect of this item of work is not susceptible of any check since details as to the size of stones used, the lead involved, the actual labour employed etc., are not noted therein. These details may be furnished.

As regards the rate of soling metal for roads, a copy of the approved data sheet and a copy of the approved schedule may be sent.

Yours faithfully,

(V.Hanumanthappa)
Asst. Secretary to Government,
L.S.G. & Planning Departments.

LNS.2.8/4.

412

(F. No. 63] **GOVERNMENT OF MYSORE**

(25) (24)

6884

27 DEC 1954 MUNICIPAL BRANCH

Telegram / phone

No. 14 30/54-5 (Encone)

Encls.

OFFICE OF The Chairman, City Improvement Trust Board, Bangalore.

Date 17th December 1954.

22

To

The Secretary to Government,
Local Self Government and Planning Departments,
Bangalore.

Sir,

23 DEC 1954 GOVERNMENT OF MYSORE

Subject:- Revised Estimate for the North Zone of Industrial Suburb.

With reference to your letter No.282 dated 12-4-54 and subsequent reminder No.L.10617 dated 4-12-54 calling for certain particulars regarding the above, I write to report as follows:-

It is reported in this Office No.4369/53-4 dated 13-1-54 that the rate of Re.0-5-6 per C.Ft. for unsize stone paving for the floor of culverts etc., was arrived at as per data, as the rate of Rs.3/- per C.Yd. sanctioned for rough stone paving which works out to 0-3-0 per C.Ft. is unworkable.

The details for size of stones used can only be furnished on average basis, since the stones used are all not uniform. The size of stones used may be of 6" x 9" x 9". The lead involved is from 7 miles (Bettahalasur Quarry). The labour employed for loading and unloading will be 4 in number and cost per trip includ. the petrol and hire charges for the lorry. Hence the rate of Re.0-5-6 per C.Ft. is admissible.

As regards the rate of soling metal for roads, a rate of Rs.5-8-0 per C.Yd. has been provided in the Schedule of rates of 49-50 and approved by Government in their Order No.L.9696-40-49-6 dated 14-3-50. Hence the data for the same has not been furnished.

A copy of the approved schedule only for roads and layout works for 1949-50 will be forwarded separately.

P.T.O.

(25)

separately.

Yours faithfully,

(D.R. Chennarudraiya)
Chairman

Ksr.

The difference in rates provided in the sanctioned and revised estimate is as follows:

Sl No.	Particulars.	Rates as per sanctioned estimate.	Schedule of Rates. Minimum.	Schedule of Rates. Maximum	Rate as per Rev. Estimate.	Total excess cost
1.	Unsize stone paving (Granite stones are used and hence the rate was passed as per the data)	5-0-0 C.Yd. 308 1540/-	5-0-0		0-5-6 C.Ft 9273 3197	1657
2.	Soling Metal for roads.	3-14-0 C.Yd. 5217 20216	5-8-0	6-0-0	5-8-0 5217 28,694	8478

S Ramappa
Chairman.
16/12/54.

6284

C. F. No. 46

GOVERNMENT OF MYSORE

No. D 562

Encls.

OFFICE OF The Chairman,
City Improvement Trust Board,
Bangalore.

Date 27th December 1954.
4th January 1955

To

The Secretary to Government,
Local Self Government and Education Departments
Bangalore.

Sir,

Subject:- Revised Estimate for the North Zone of Industrial Suburb.

In continuation of this Office letter No.1430 dated 22-12-54 furnishing certain particulars regarding the above I write to forward herewith a copy of scheduled items for "Roads" only, approved in Government Order No.L.9696/40-49-6 dated 14-3-50 for information.

Yours faithfully,

D.R. Chennarudraiya

(D.R. Chennarudraiya)
Chairman.

30/12/54.

Continued

(28)

CITY IMPROVEMENT TRUST BOARD BANGALORE

Aproved Schedule of rates for the year 1949-50 for Road works only.

	Item of work.	Per	Minimum Rate Rs P	Maximum Rate Rs A P
1	Collecting conveying and Stacking granite metal to 1½" Size including breaking and lead etc Complete	Cyd	9 0 0	10 0 0
	—do— 1¼" to ¾" —— do ——	"	10	12 0 0
2	—do— Soling metal granite on broken metal 3" to 4" Sizes including lead etc complete		6	
	—do—		5 8 0	
3	Collecting, Conveying and Stacking of gravel at the spot including lead		3 0 0	3 8 0
4	Picking and forming the metalled Surface —	Syd	0 0 9	
a)	—do— gravelled Surface	"	0 0 4	
5	Spreading the metal and hand packing.	Cyd	0 4 0	
a)	—do— gravel		0 3 6	
	—do— Sand		0 3 0	
6	Consolidation of metal by Stone road roller including watering and spreading and Consolidation by Stone road roller		0 8 0	
*	Spreading and hand packing and Consolidation of Surface metal by power road roller		1 4 0	
a)	Consolidation of metal by Steam road Roller		1 4 0	
b)	—do— Gravel by Stone road-roller		0 4 0	
	Spreading and Consolidating Soling metal by P.K.R. including watering		1 2 0	
7	Excavating pit Gravel including spreading & consolidating etc complete		0 14 0	
8	collecting & Spreading B. Kumbalgud 2 to 3 miles		3 8 0	
a	Collecting, Stacking & spreading & consolidating gravel including watering			
B	watering charges during consolidation time with a lead of 2 furlongs		0 7 6	

29

10	Excavating check drains, shoulder drains &				
---	Side drains & forming the excavated earth	Cyd	0 10 0		
a	forming foot paths		0 10 0		
11	Excavation (in cutting) in ordinary soil		0 4 0	0 5 0	
a	—do— in all kinds of soil & using the stuff to forming the foot paths & at sides of roads for small depths		0 6 0		
b	—do— in cutting in new formations deepen depth		0 10 0		
c	filling foot paths with available earth forming and consolidating		0 6 0		
d	—do— in hard rock (by blasting		8 0 0		
e	—do— in hard rock (by chisselling		12 0 0		
12	Forming embankment by using the excavated stuff including lead etc complete		0 6 0		
13	Turfing the embankment including lead	Sq.yd	0 2 0	2 6	
14	providing rough stone revetment with selly with one mile lead	Cyd	2 8 0	0 0	
15	Deepening the drains and using the stuff for The road	C.yd	0 5 0		
16	Deepening the side and shoulder drains in all sides	"	0 6 0		
17	Clearing side and shoulder drains for 3" to 4" Depth	R.Yd	0 0 6		
a	—— do —— Below 3"		0 0 3		
18	Removing and stacking loose metal on the road surface	Fur	0 6 0		
19	Removing lantana bushes Thickly grown on road sides together with roots etc complete	Sq.yd	0 0 6		
a	—— Do —— Thickly grown —do—		0 0 9		
b	—— Do —— Thin Jungle	Ft	1 8 0		
20	Gravel blindage over the exposed metal surface		3 10 0	3 8 0	
a	Sand blindage A		2 8 0	3 0 0	
21	Scraping grass	Sq.yd	0 0 1	0 0 2	

(31)

			Rs	As	Ps	Rs	As	Ps
30	Earth work for preparing plat forms for slabbing	Syd	0	0	2			
2.	providing & fixing burnt stone (Size stone) road metal around the plat forms to indicate boundary	each	0	1	6			
31	Burnt stone slabs 3" Thick including fixing	Sft	0	7	0			
a.	— do — 4½" Thick — do — etc complete	"	0	9	0			
b.	— do — 6" Thick — do	"	0	12	0			
c	— do — 9" Thick — do —		1	0	0			
32	Breaking rock		0	6	0			
33	Dry stone dwarf wall on side of road to Serve as parapet with Size stone with lead & lift	Cyd	2	8	0			

"Copy"

Approved in G.O. no L 9696/40-49-6/ Dated 14-3-50

NB — * For Jayanagar and its Surroundings

÷ For Industrial Suburb North Approved by the board Vide resolution dated 21.12.48

Engineer Officer, 3/1/53
City Improvement Trust Board
Bangalore.

30/1/53

Aprroved Schedule of rates for the year 1949 – 50 for Road works only (Continued)

(30)

22	Supplying and fixing new mile stones as per type design with painting etc complete	Each	12 0 0
a	— Do — Big Size — do —		15 0 0
23	Supplying fixing new furlong stones as per type design with painting		5 0 0
24	Supplying and fixing tunnel no stones as per design with painting		1 0 0
25	Supplying and fixing guard stones		1 8 0
26	Supplying and fixing boundary stone as per type design including painting and figuring etc complete		15 0 0
27	Providing and fixing Finger post (Stone) as per type design including figuring and painting		120 0 0
a	— Do — Without figuring and painting		90 0 0
b	painting letters in the finger post	Each	0 1 0
28	Removing & refixing the mile stone including painting etc complete		1 8 0
a	— Do — furlong stone		0 9 0
b	— Do — Tunnel no stone		0 6 0
c	— Do — boundary stone		1 8 0
d	— Do — finger post		5 0 0
29	Cutting letters in stone slabs — 1" size		0 2 6
a	— Do — " — 1½" — " —		0 3 0
b	— Do — " — 2" — " —		0 3 6
c	— Do — " — 2½" — " —		0 4 0
d	— Do — " — 3" — " —		0 4 6
e	— Do — " — 4" — " —		0 5 0
F	— Do — " — 6" — " —		0 8 0

(32)

C. F. No. 45] **GOVERNMENT OF MYSORE**

8830

Telegram / phone

OFFICE OF

the Chairman, City Improvement Trust Board, Bangalore,

No. 7914/Su.r

Encls

Date 26th February 1955.

To

The Secretary to Government,

Local Self-Government and Education Departments,

Bangalore

JGB. 13 55 12

Regarding:- Revised Estimate for the North Zone of the Industrial Suburb, Bangalore.

Inviting kind referance to my letter No.G.228/51-52 dated the 7th June 1951 and subsequent correspondence ending with my letter No.A2.P.R.320/53-4 dated the 31st August 1953, regarding the above, and forwarding there with an estimate amounting to Rs.14,30,556/- for the above work, I request you to kindly arrange to return the same duly sanctioned very early.

The revised estimate includes a provision of Rs.1,55,000/- for laying water supply Sub mains as per estimate received from the water supply Division, Bangalore.

In this area a number of Factories etc., are already coming up, and the owners due to ~~non~~supply are put to considerable inconvenience for want of water facility, which can only be done if the sub mains are laid and served. Under the circumstances, I request you to kindly communicate Sanction of Government to the estimate or approval to push through this work pending sanction to the revised estimate immediately.

Yours faithfully,

(D.R. Chennarudraiya)

Chairman.

jk)

1/6
ew pleased
~~[illegible]~~ with Trial
No. 9/13.
25.49-54

Im - approved draft

Appendix F.G.—1]

(33)

SUBJECT .....

.....

.....

Diary No. of letter replied to.....

Section

File No.

Serial No.

Mysore Government Secretariat

( )

the *195*

Date of issue.....

Signed by..... H

J

List of enclosures.....

Copied by.....

Examined by.....

No.

To

Proceedings

Read: -

1) GO NL 4781-7/NL 171-48-2 d 5/11/1948 according sanction to the scheme for the formation of ~~2 Industrial~~ Northern Zone of the Industrial suburb, Bangalore at an estimated cost of Rs 8,21,600

2) ~~GO NL~~ Letter NO L 9686/J.T.B 40-49-6 & 14-3-50 affirming the schedule of rates for works in the C.J.T.B, Bangalore, during the year 1949-50:

3) Correspondence ending with letter NO 7914/52-5 d $\frac{26}{28}$-2-55 from the

chairman, C.I.T.B, Bangalore forwarding a revised estimate for Rs 14,30,556 for the scheme ~~referred to~~ sanctioned in the G.O. read above dated 5-11-48

3) Unofficial note No 11308/R.B 54-55 dated 5-8-55 of the Deputy C.E. on the subject ~~the Judge returning the estimate duly scrutinised and enclosed.~~

STATEMENT

The cost of the scheme is reported to have been revised for the following reasons:- Vide page

(1) the cost for the formation of roads has been revised to Rs 4,39,442/- as against the sanctioned provision of Rs 3,10,665/-, the excess being on account of higher rates paid for certain items of work such as earth work and soling metal.

(2) Due to the modification in the alignment of 40' road between Yeswant Soap Factory, during execution

Appendix F.G.—1]

(35)

SUBJECT .....

.....

.....

Diary No. of letter replied to.....

Mysore Government Secretariat

( )

the *195*

Date of issue.....

Signed by.....

List of enclosures.....

Copied by.....

Examined by.....

Section

File No.

Serial No.

No—

~~To~~

(3) A width of 18' has been adopted for metalling of roads instead of 16' as provided in the sanctioned estimate

(4) A rate of Rs 5-8-0 per c.yd has been provided for supplying of stone metal as against the rate of Rs 3-12-0 provided in the sanctioned estimate

(5) The cost of inaugural pillar as also the cost of forming a park abroad has been included

(6) Provision towards the cost of acquisition has been revised to Rs 5, 70, 114/- as against the sanctioned provision of Rs 3, 55, 971.

(30)

(7) A ~~sum of Rs 2000/-~~ premium of Rs 2,66,000 towards conversion fine to be paid at Rs 2000 per acre has been made

14 sites are reported to have been formed A sum of Rs 19,27,917/- is expected to be received from sale of sites in the area

~~The Deputy C.E. has sanctioned the estimate and~~ The estimate for Rs 14,30,556/- received from the Chairman, C.J.T.B, Bangalore has been scrutinised by the Deputy C-E and corrects to Rs 14,27,000 with observations of the following, ~~remarks~~;-

(a) } V.S. Please type here Para 49 (for 'a')
(b) } Para 50 (for 'b')

~~are~~ agree with the Deputy C.E. and they accordingly sanction the estimate for Rs 14,27,000 as scrutinised by him

To, The Chairman, C.J.T.B, Bangalore ~~VR~~
The C-E,
The D.C. Bangalore Dist
~~The~~
The Executive S.A.D.

Yours faithfully

DRAFT. ITB. 13. SS 57/12

PROCEEDINGS OF THE GOVERNMENT OF MYSORE.

-O-

Read:-

Government Order No.L. 4781-7/Ml.171-48-2 dated 5-11-1948, according sanction to the scheme for the formation of Northern Zone of the Industrial Suburb, Bangalore, at an estimated cost of Rs.8,21,600.

2. Letter No.L.9696/ITB.40-49-6 dated 14-3-50 approving the schedule of rates for works in the City Improvement Trust Board, Bangalore, during the year 1949-50.

3. Correspondence ending with letter No. 7914/54-55 dated 26/28-2-1955, from the Chairman, City Improvement Trust Board, Bangalore, forwarding a revised estimate for Rs. 14,30,556/- for the scheme sanctioned in the Government Order dated 5-11-48.

4. Unofficial Note No. 11308/R.B.54-55 dated 5/8-2-1955 of the Deputy Chief Engineer of Mysore, on the subject.

***

ORDER NO. L. 3016-20/ITB 13-SS-12

DATED, BANGALORE, THE 18 JUNE 1955.

The cost of the scheme is reported to have been revised for the following reasons.

(1) The cost for the formation of roads has been revised to Rs. 4,39,442/- as against the sanctioned provision of Rs.3,10,665/- on account of higher rates paid for certain items of work such as earth work and soling metal.

(2) due to the modification in the alignment of 40' road behind Yeswant Soap Factory during execution;

(3) A width of 18' has been adopted for metalling of roads instead of 16', as provided in the sanctioned estimate.

(38)

(4) A rate of Rs. 5-8-0 per C.yd. has been provided for supplying of soling metal, as against the rate of Rs. 3-12-0 provided in the sanctioned estimate;

(5) The cost of Inaugural Pillar ~~as also the cost~~ and cost of forming a park alround has been included.

(6) Provision towards the cost of acquisition has been revised to Rs. 5,70,114/- as against the sanctioned provision of Rs. 3,55,971.

(7) A provision of Rs. 2,66,000/- towards conversion fine to be paid at Rs. 2,000/- per acre has been made.

(2) 148 Sites are reported to have been formed. A sum of Rs. 19,27,917/- is expected to be received from sale of sites in the area. The estimate for Rs. 14.30.556/- received from the Chairman, City Improvement Trust Board, Bangalore, has been scrutinised by the Deputy Chief Engineer and corrected to Rs. 14,27,000/- with the following observations:-

(a) It is seen that a rate of Re.0-5-6 per Cft. or Rs. 9-4-6 a cyd. is provided for unsized stone paving in the estimate. The approved schedule of the City Improvement Trust Board for the year 1951-52, provided for this item of work a rate of Rs. 3/- per cyd., which is also the rate provided for in the schedule of Buildings Division, Bangalore, for the year 1950-51-52. As a special case, the rate originally provided in the estimate i.e., Rs. 5/- per c.yd. has been admitted and nothing more than this is admissible.

(b) With regard to soling metal for roads a rate of Rs. 5-8-0 per cyd. is provided for in the estimate and this rate is retained as it is stated to have been ap-

D/11-6/52

approved by Government in their order No. L.9696/ITB.40-96-6 dated 14-3-1950.

Government agree with the Deputy Chief Engineer and they accordingly sanction the estimate for Rs. 14,27,000/- as scrutinised by him.

Secretary to Govennment,
Education & L.S.G.Departments.

TO

The Chairman, City Improvement Trust Board, Bangalore,w/r.
The Chief Engineer of Mysore, Bangalore.
The Deputy Commissioner, Bangalore District.
The Controller, State Accounts Department, Bangalore.

HGN.dft./7-6.

(40)

PROCEEDINGS OF GOVERNMENT OF MYSORE

-:-

SUBJECT:-

Government Order No.L.4781-7/Al.171-48-2 dated 5-11-1948, according sanction to the scheme for the formation of Northern Zone of the Industrial Suburb, Bangalore, at an estimated cost of Rs.8,21,600/-

2. Letter No...9696/ITB.40-49-6 dated 14-3-1950 approving the schedule of rates for works in the City Improvement Trust Board, Bangalore, during the year 1949-50.

3. Correspondence ending with letter No.7914/54-55 dated 26/28-2-55 from the Chairman, City Improvement Trust Board, Bangalore, forwarding a revised estimate for Rs.14,30,556/- for the scheme sanctioned in the Government Order dated 5-11-1948.

4. Un-official Note No.11308/...3.54-55 dated 1/3-7-1955 of the Deputy Chief Engineer of Mysore, on the subject.

* * * *

ORDER No.L. 3016-20/113 13-55-12

Dated, Bangalore, the 18-6-55

The cost of the scheme is reported to have been revised for the following reasons:-

i) the cost for the formation of roads has been revised to Rs.4,39,442/- as against the sanctioned provision of Rs.3,19,665/- on account of higher rates paid for certain items of work such as earth work and soling metal;

ii) due to the modification in the alignment of 40' road behind Yesvant Soap Factory during execution;

iii) a width of 18' has been adopted for metalling of roads instead of 16', as provided in the sanctioned estimate;

iv) a rate of Rs.5-8-0 per C.yd. has been provided for supplying of soling metals against the rate of Rs.3-12-0 provided in the sanctioned estimate;

v) the cost of Inaugural Pillar and of forming a park ground has been included;

vi) provision towards the cost ofacquisition has been revised to Rs.5,70,114/- as against the sanctioned provision of Rs.2,55,971/-;

vii) a provision of Rs.2,66,000/- towards conversion fine to be paid at Rs.2,000/- per acre has been made.

2. 148 sites are reported to have been formed. A sum of Rs.19,27,917/- is expected to be received from sale of sites in the area. The estimate for Rs.14,30,556/- received from the Chairman, City Improvement Trust Board, Bangalore, has been scrutinised by the Deputy Chief Engineer and corrected to Rs.14,27,000/- with the following observations:-

a) it is seen that a rate of Rs.0-5-6 per c.ft or Rs.4-4-0 per c.yd is provided for unsel d stone pavin in lieu of t . e

approved as schedule of the City Improvement Trust Board for the year 1951-52 provides for this item of work a rate of Rs.3/- per cyd., which is also the rate provided for in the schedule of Buildings Division, Bangalore, for the year 1950-51-52. As a special case, the rate originally provided in the estimate i.e., Rs.5/- per cyd. has been admitted and nothing more than this is admissible.

b) with regard to soling metal for roads a rate of Rs.5-8-0 per cyd. is provided for in the estimate and this rate is retained as it is stated to have been approved by Government in their order No.L.9696/ITB. 40-96-6 dated 14-3-1950.

3. Government agree with the Deputy Chief Engineer and they accordingly sanction the estimate for Rs.14,27,000/- as scrutinised by him.

(V.Hanumanthappa)
for Secretary to Government,
Education & L.S.G.Departments.

To

The Chairman, City Improvement Trust Board, Bangalore with records
" Chief Engineer of Mysore, Bangalore,
" Deputy Commissioner, Bangalore District,
" Controller, State Accounts Department, Bangalore.

knr-7/15.6
